

# Introduction

Tobias Haas

8 Sep 2017

---


## Phase II Cabling SASE3/SASE2



2

- First version of cable list was given to Actemium on Thursday
  - Unfortunately Actemium did not use the provisional list by EETF sent in June to order missing connectors and cables
  - This is unfortunate since we know now that there will be more cables in SASE3 than there are in SASE1
  - Actemium does not have an up-to-date list of their inventory
  - This could lead to additional delays...
- The Phase II cabling contract was tendered
  - Submission date is 27 September

## Phase I Cabling SASE2/3



- Works in SASE3 are not making progress currently
- Meeting with VATER yesterday
  - Start again next week
  - Will send new time schedule
  - Racks for SASE2 arrive next week (11 Sep)
- Work in SASE2 is supposed to start in October
  - This is unlikely as SASE3 work will not be finished
  - This is currently not critical

# Crane and AC installations in SCS




# Little progress with Phase I Cabling in SCS






# Signal Cabling of LPD in FXE

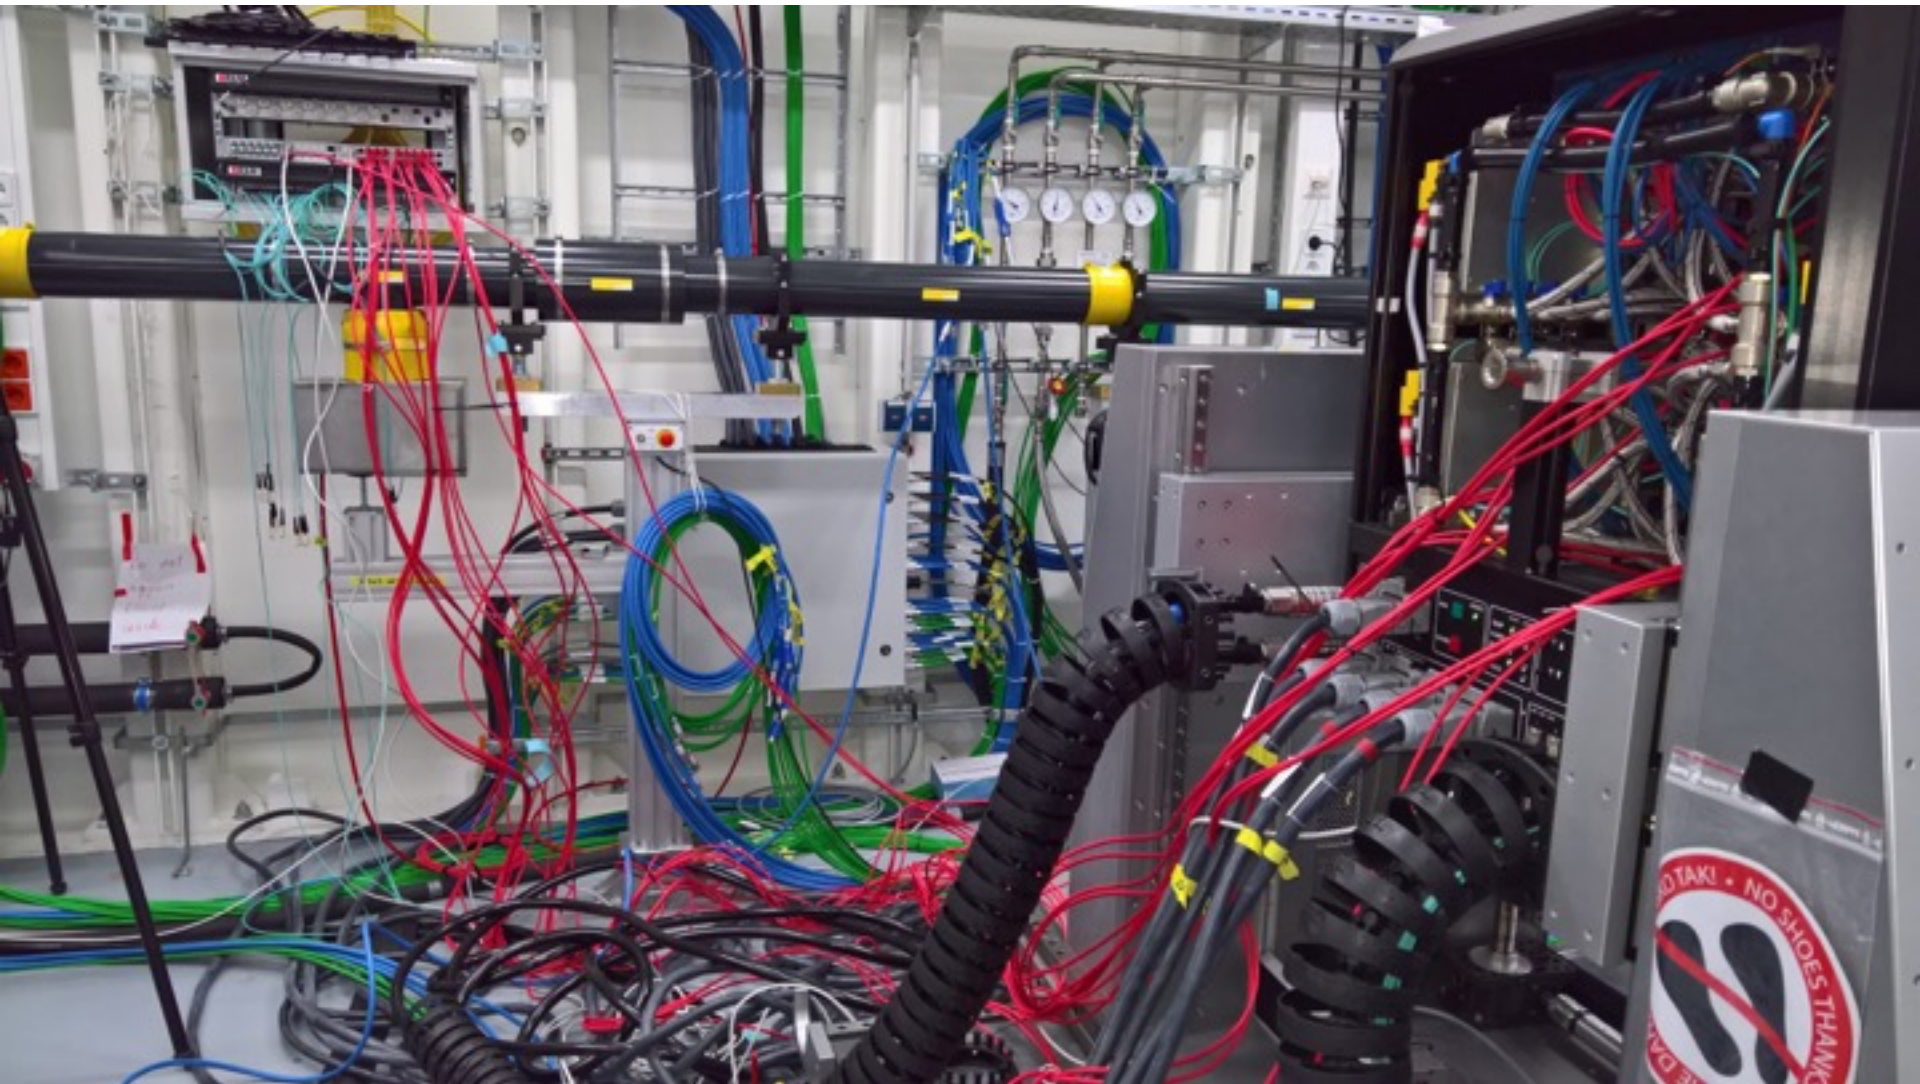


# Preparation of Laser Beam Transport in FXE





# Finished Double Floor being covered in A23/HED



8






# Cooling Water Pumps in SASE2




# Progress with beam line installations XTD6






# Progress with beam line in XTD6

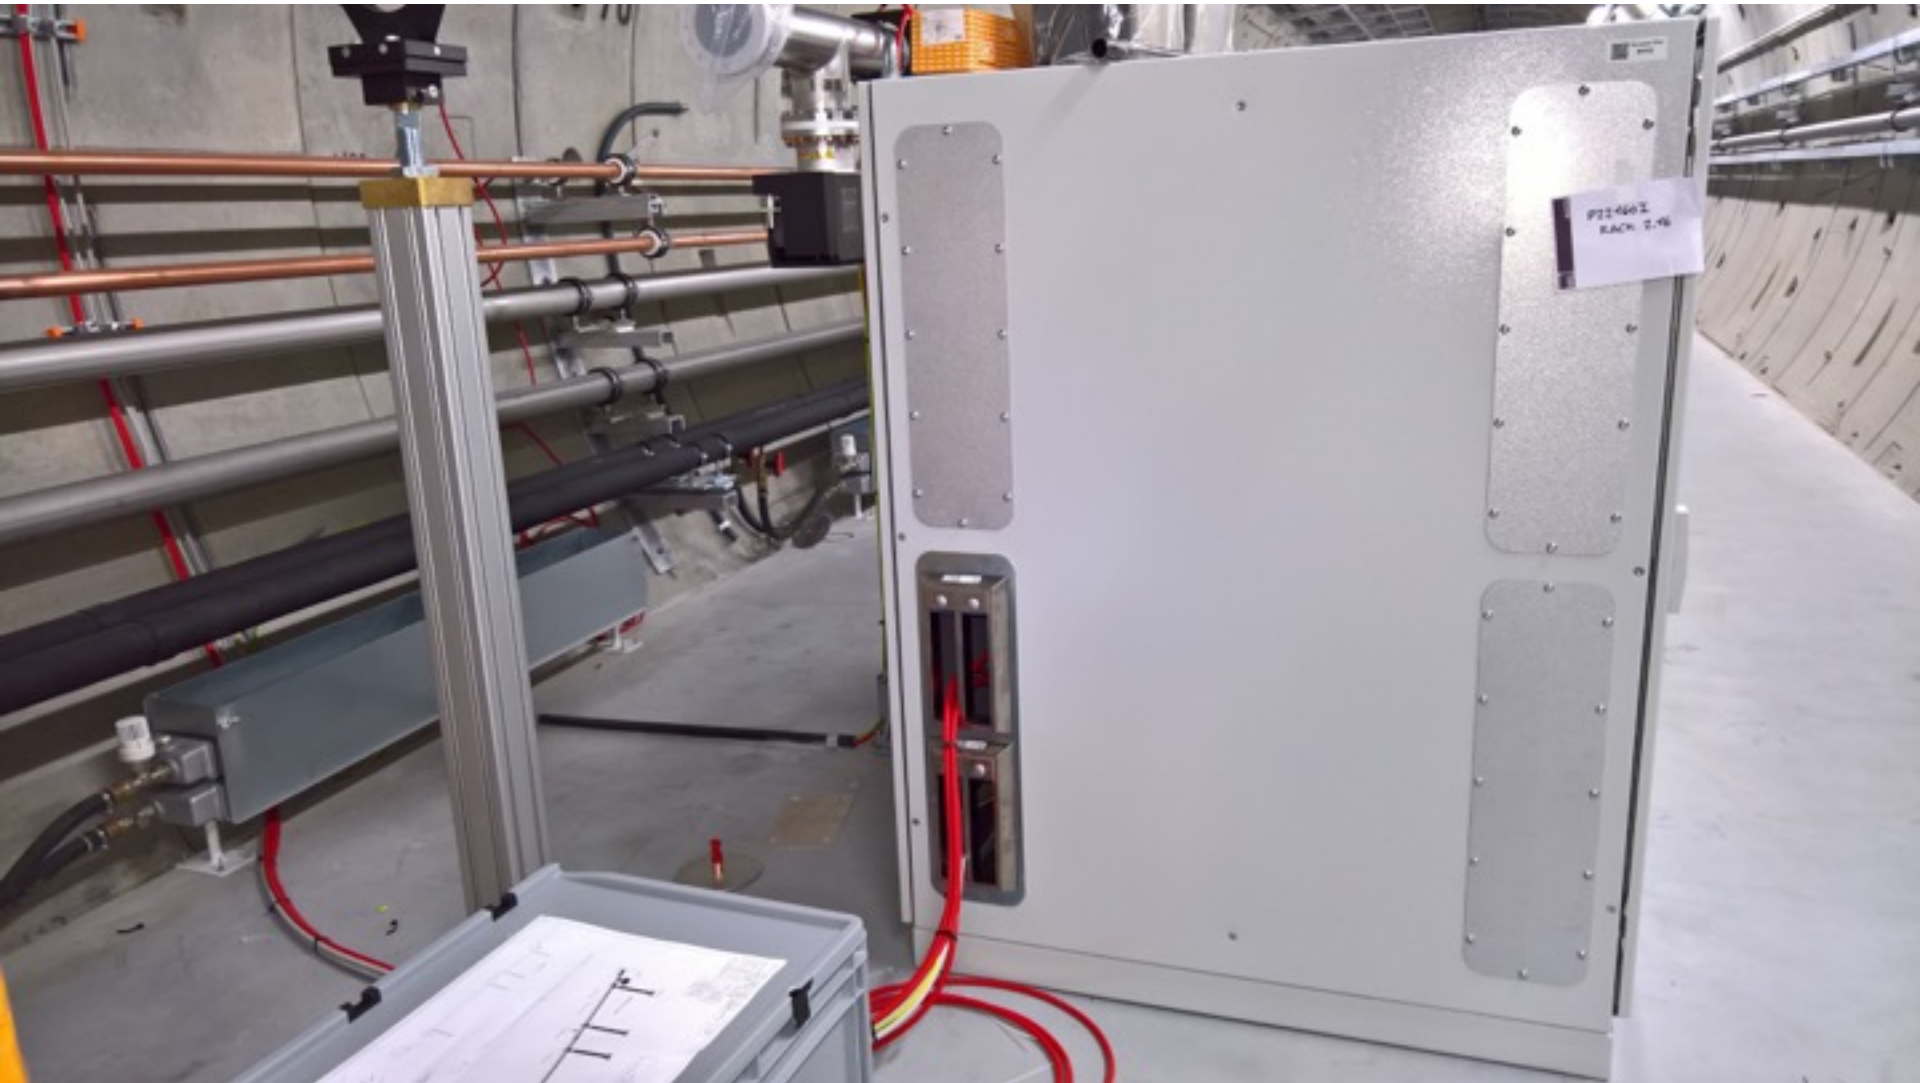




# Progress with beam line in XTD1



## Next Meetings



- 09:00: SASE1/3 Readiness
- Mo/Wed 09:30: SASE1/3 Readiness Dispatch
- Friday, 15 Sep: XHEXP1 Coordination
  - Roadmap for SASE2/3 Completion
