ID	Task Name
1	**SASE 1: FXE/SPB**
2	Requ.document FXE
3	E-plan design
4	Production IKC
5	Requ. document SPB
6	E-plan design
7	Production IKC SPB
8	**SPB pending req. document**
9	**Req. document SPB**
23	Approval process(CAS, AE)
24	E-plan design
25	Production
26	Day 1 Electronics done
27	Delivery, acceptance
28	Delivery
29	Acceptance Test
30	**Phase I Cabling**
34	**PII Cabling**
35	Delivery cables
36	Manufacturing
37	FXE Installation
38	SPB Installation
39	Decision to extend Actemium contract
40	Frame installation
41	Beckhoff Installation in racks
42	Ready to test crates
43	Test crates with sim. boxes
44	Test crates with BL_HW
45	**SASE 3: SCS/SQS**
46	Kick off
47	Requ. document SCS
48	Requ. document SQS
49	Cabling List for PII cabling
50	Phase II cabling production documentation
51	E-plan design
52	Production IKC
53	Day 1 Electronics done
54	Delivery

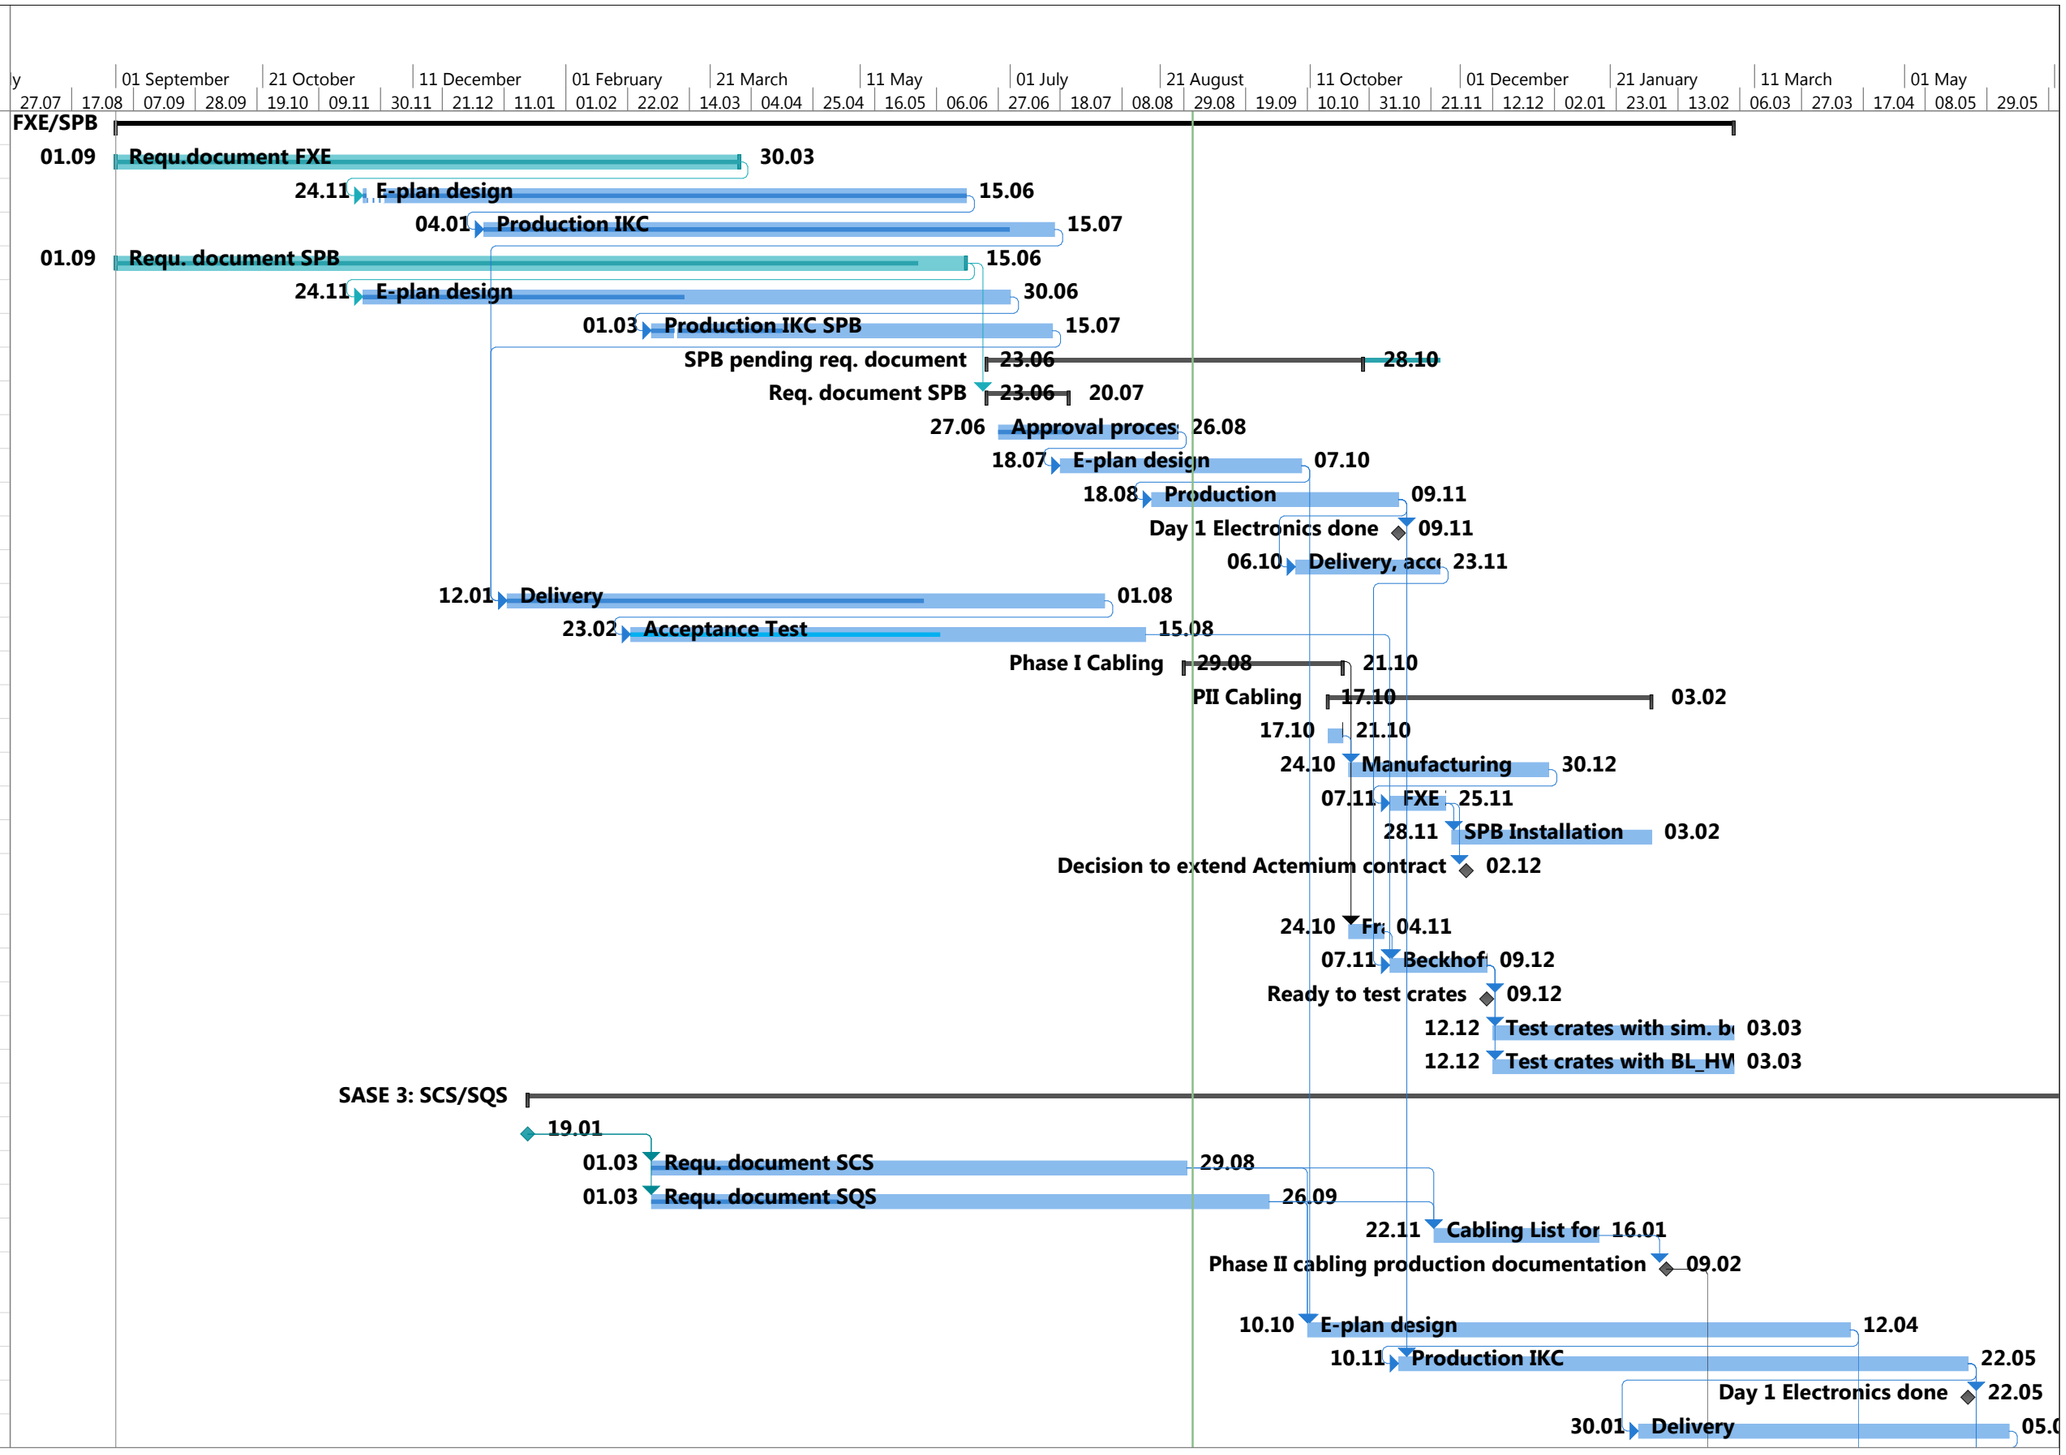

Project: Project_FXE
Date: Thu 01.09.16

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name
55	Acceptance Test
56	Phase I cabling
57	Phase II cabling
58	Installation in racks
59	Ready to test crates
60	
61	**SASE 2: MID/HED**
62	Kick off
63	Requ. document MID
64	Requ. document HED
65	Cable list for PII cabling
66	Phase II cabling production documentation
67	E-plan design
68	Production IKC
69	Day 1 electronics done
70	Delivery
71	Acceptance Test
72	Phase I cabling
73	Phase II cabling
74	Installation in racks
75	Ready to test crates
76	**FXE/SPB/SQS/SCS Low Priority**

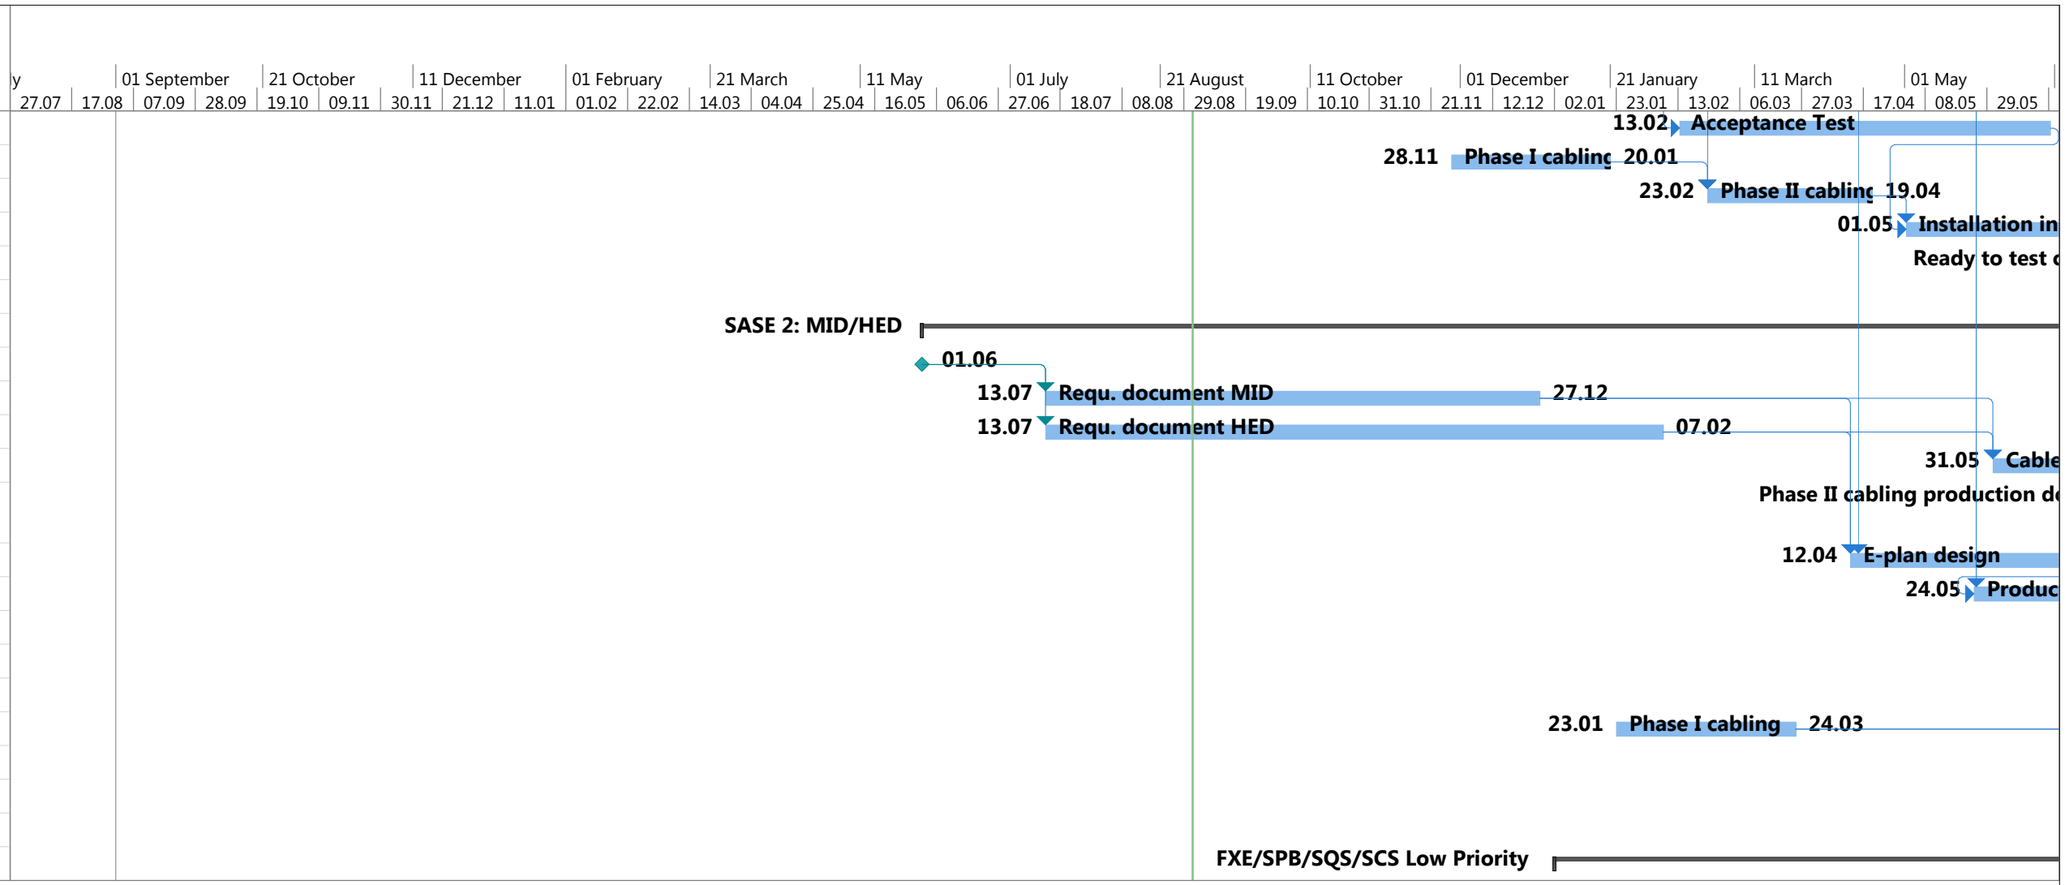

Project: Project_FXE
Date: Thu 01.09.16

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

75 Ready to test crates

Ready to test crates
